



Aspect Weekly Update

Seven Acres Development (Former LDM Site - ECSI #887)


WEEK 47: SEPTEMBER 5 - SEPTEMBER 9, 2022

ON-SITE ACTIVITIES

- Began ROW electrical work.
- Parcel 1:
 - Continued backfilling Garage 1 and NE Retaining Wall.
 - Continued constructing Buildings 1, 2, 3, and 4.
 - Continued radon piping for Building 5; prepared and poured slab-on-grade.
- Parcel 2:
 - Clubhouse MEP rough-ins.
 - Continued Garage 2 grade preparation for vapor barrier installation.
 - Began Garage 2 vapor barrier installation.
 - No waste was transported off site this week.
- Aspect was on site on 9/9.

PLAN VIEW PROGRESS

Parcel 2 construction work focused on Garage 2 grade preparation and vapor barrier installation.

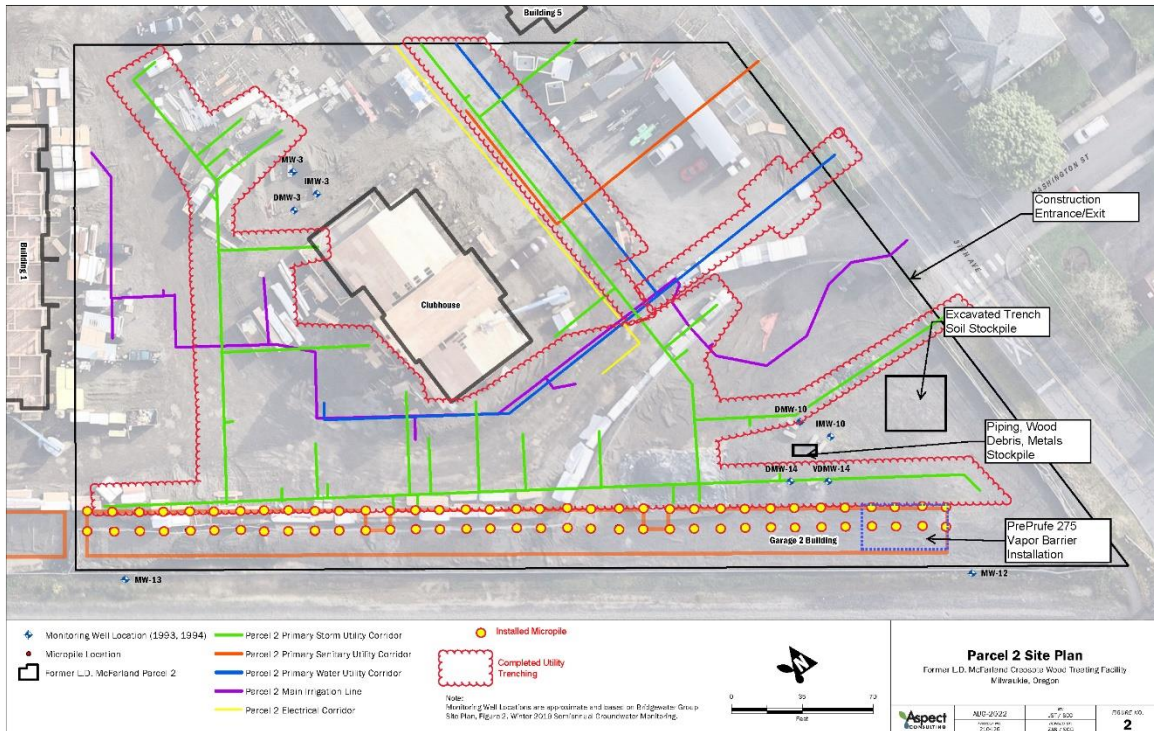

KEY ONSITE ACTIVITIES PLANNED FOR NEXT TWO WEEKS

- Begin ROW signage, striping and irrigation mains.
- Parcel 1:
 - Continue Garage 1 backfill. Garage 1 building pad prep.
 - Continue construction for Buildings 1, 2, 3, and 4.
 - Continue Building 5 slab-on-grade pour. Begin wall framing and floor joists for Building 5.
- Parcel 2:
 - Continue Clubhouse MEP rough-ins. Begin drywall hanging and insulation.
 - Continued Parcel 2 excavation for utilities, stockpiling excavated soil.
 - Holt Drilling to adjust the seven Parcel 2 monitoring wells to be closer to finished grade, on 9/12 and 9/13.
 - Continue Garage 2 vapor barrier installation. Begin Garage 2 concrete foundations installation. Aspect will keep DEQ apprised of schedule.
 - Place stockpiled excavated soil as backfill beneath designated Parcel 2 parking areas.

UPCOMING DELIVERABLES to DEQ and ACTION ITEM REQUESTS

- None.

PHOTOS



9/9/22 Parcel 2 Garage 2 subgrade preparation for vapor barrier installation.



9/9/22 Start of Parcel 2 Garage 2 Vapor Barrier installation.
