



Aspect Weekly Update

Monroe Street Apartments Development (Former LDM
Site - ECSI #887)


WEEK 15: JANUARY 24 - JANUARY 28, 2022

ON-SITE ACTIVITIES

- Continued preparation of foundation and general utilities for Building 1 on Parcel 1.
- TerraCalc surveyed ROW utilities.
- ACS was on site to inspect stem wall footings.
- Building 1 stem walls were poured.
- No analytical samples were collected this week.
- No waste was transported off site this week.

PLAN VIEW PROGRESS

Construction work focused on Building 1 area on Parcel 1.

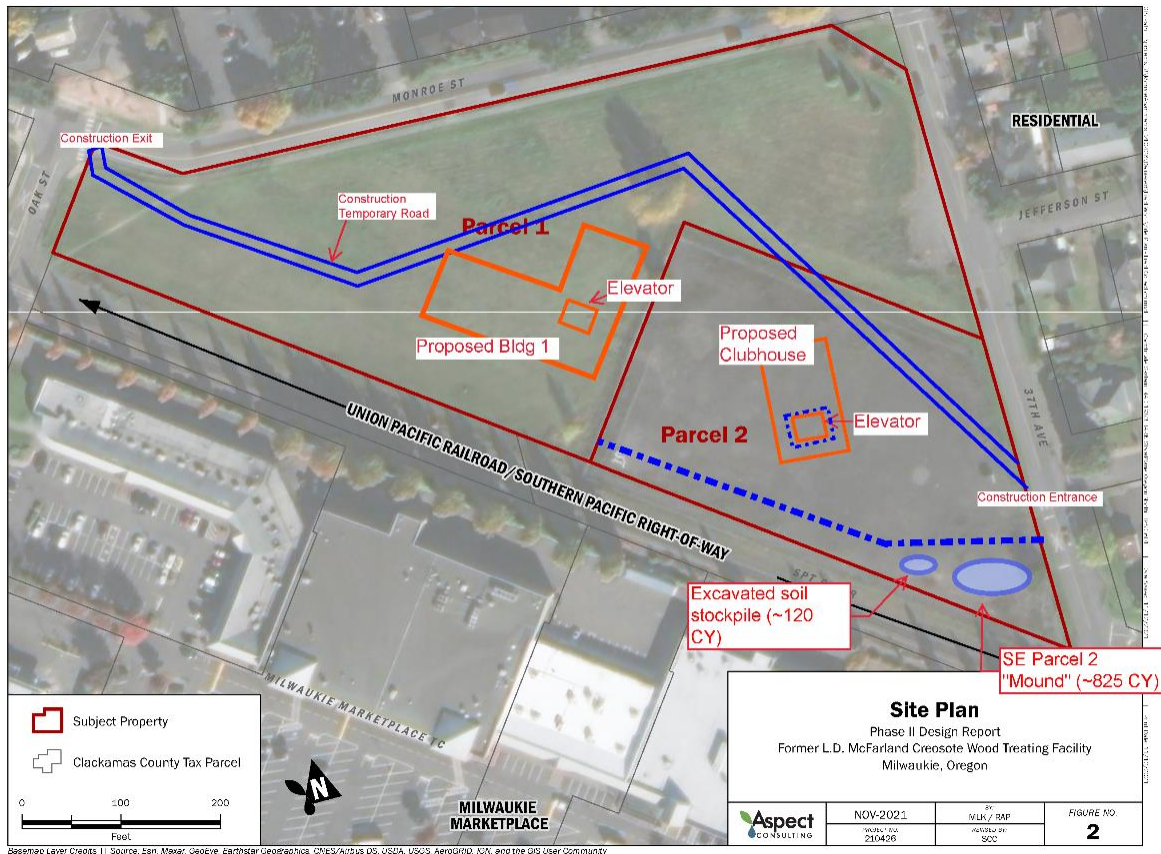

KEY ONSITE ACTIVITIES PLANNED FOR NEXT TWO WEEKS

- Excavate and prepare interior footings, radon mitigation system, and general utilities for Building 1.
- Prepare Clubhouse elevator pit for waterproofing and vapor barrier. DEQ will be notified before any vapor barrier placement.
- Bury Parcel 2 mound soil and excavated soil stockpile as Parcel 2 fill beneath the clean fill cap, where structurally possible, to minimize offsite soil disposal.

UPCOMING DELIVERABLES to DEQ and ACTION ITEM REQUESTS

- Winter 2022 semiannual groundwater monitoring report will be submitted in February.
- Vapor barrier detail for Clubhouse elevator pit area will be provided to DEQ.

PHOTOS



1/27/22 Clubhouse area on Parcel 2, looking south. Elevator pit in background, fenced off. Stockpiled excavated Parcel 2 soil in far background.



1/27/22 Backfilling underground plumbing at Building 1 on Parcel 1, looking north.
