



Aspect Weekly Update

Monroe Street Apartments Development (Former LDM
Site - ECSI #887)

WEEK 27: APRIL 18 - APRIL 22, 2022


ON-SITE ACTIVITIES

- Continued working on site utilities (water, storm, sanitary).
- Continued PGE utility/infrastructure work.
- Parcel 1:
 - Continued framing for Buildings 1 and 2, and mock-up.
 - Continued preparation for Building 3 perimeter footings/stem walls and plumbing.
 - Continued preparation of Building 4 footings.
- Parcel 2:
 - Continued framing for Clubhouse.
- Point Environmental was on site on 4/20 to inspect erosion control measures.
- No analytical samples were collected this week.

- No waste was transported off site this week.

PLAN VIEW PROGRESS

Construction work focused on Buildings 1 to 4 on Parcel 1, and on the Clubhouse on Parcel 2.

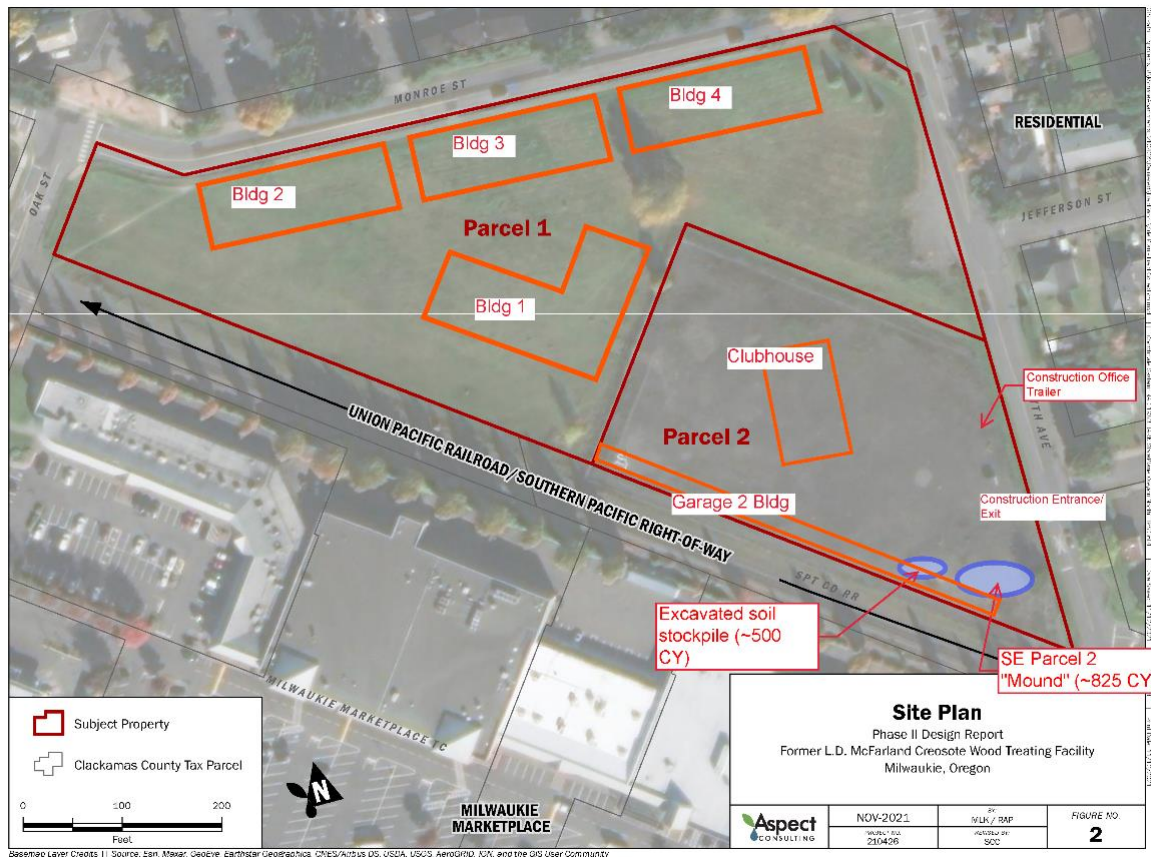

KEY ONSITE ACTIVITIES PLANNED FOR NEXT TWO WEEKS

- Continue site utility work (water, storm, sanitary).
- Continue PGE utility/infrastructure work.
- Parcel 1:
 - Continue mock-up construction.
 - Continue framing and floor joists/decking for Buildings 1 and 2.

- Continue preparation for Buildings 3 and 4 perimeter footings/stem walls and plumbing, and radon/slab on grade.
- Parcel 2:
 - Continue Clubhouse framing.
 - Begin Garage 2 retaining wall excavation, pending City approvals. DEQ approved the Garage 2 foundation redesign on 4/6.

UPCOMING DELIVERABLES to DEQ and ACTION ITEM REQUESTS

- None

PHOTOS



4/20/22 Building 2 (Parcel 1), looking east.



4/20/22 Clubhouse (Parcel 2), looking southeast.
