



Aspect Weekly Update

Monroe Street Apartments Development (Former LDM
Site - ECSI #887)


WEEK 32: MAY 23 - MAY 27, 2022

ON-SITE ACTIVITIES

- Continued Parcel 1 PGE utility/infrastructure work.
- Parcel 1:
 - Continued mock-up construction.
 - Continued framing for Buildings 1, 2, and 3.
 - Continued preparation of plumbing for Building 4.
- Parcel 2:
 - Continued roofing prep for Clubhouse.
- No analytical samples were collected this week.
- No waste was transported off site this week.

PLAN VIEW PROGRESS

Construction work focused on Buildings 1 to 4 on Parcel 1, and on the Clubhouse on Parcel 2.

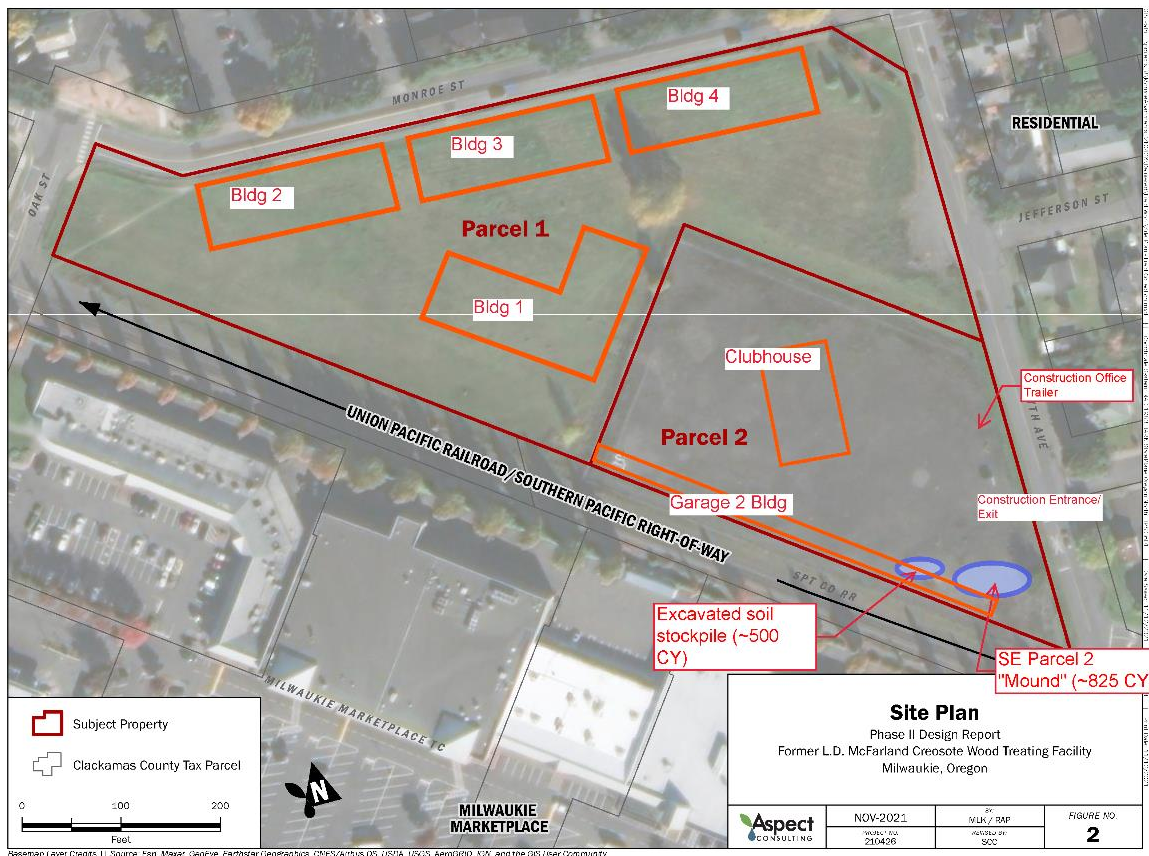

KEY ONSITE ACTIVITIES PLANNED FOR NEXT TWO WEEKS

- Continue PGE utility/infrastructure work on Parcel 1.
- Parcel 1:
 - Continue mock-up construction.
 - Continue framing and/or trusses for Buildings 1, 2, and 3.
 - Continue preparation for Building 4 radon/slab on grade.
 - Pour Building 4 slab.
- Parcel 2:
 - Continue Clubhouse roofing.
 - Garage 2 retaining wall excavation is tentatively scheduled to start on 5/31. Micropile installation is anticipated to begin in July. Aspect will keep DEQ apprised of schedule.

UPCOMING DELIVERABLES to DEQ and ACTION ITEM REQUESTS

- None

PHOTOS



5/27/22 Clubhouse (Parcel 2), looking west.



5/27/22 Building 2 in background and Building 3
in foreground (Parcel 1), looking northwest.
