



Aspect Weekly Update

Seven Acres Development (Former LDM Site - ECSI #887)


WEEK 46: AUGUST 29 - SEPTEMBER 2, 2022

ON-SITE ACTIVITIES

- ROW curbs, sidewalk and approaches.
- Parcel 1:
 - Constructed and poured north retaining wall.
 - Poured Garage 1 retaining wall.
 - Continued constructing Buildings 1, 2, 3, and 4.
 - Constructed underground utilities and radon piping for Building 5.
- Parcel 2:
 - Clubhouse MEP rough-ins.
 - Continued Parcel 2 excavation for utilities, stockpiling excavated soil.
 - Pacific Foundation proof-tested micropiles AM-34, AM-44, and AM-56, and installed micropiles AM-68 to AM-70.
 - Surveyed and cut micropiles to prep for vapor barrier placement.
- Aspect was not on site this week.
- No waste was transported off site this week.

PLAN VIEW PROGRESS

Parcel 2 construction work focused on Garage 2 micropile installation and utility trenching.

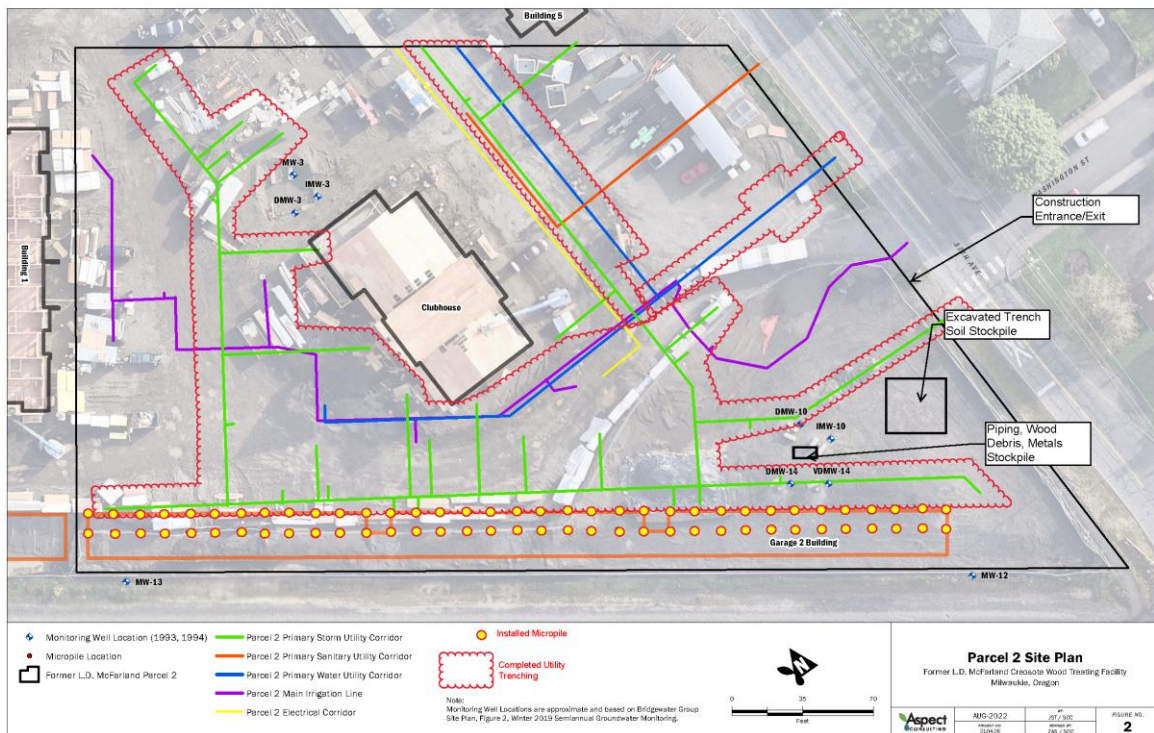


KEY ONSITE ACTIVITIES PLANNED FOR NEXT TWO WEEKS

- Continue ROW curbs, sidewalk and approaches. Begin electrical ROW work.
- Parcel 1:
 - Continue backfilling beneath Parcel 1 garage. Begin Garage 1 building pad prep.
 - Continue construction for Buildings 1, 2, 3, and 4.
 - Continue radon piping for Building 5; prepare and pour slab-on-grade.
- Parcel 2:
 - Continue Clubhouse MEP rough-ins. Begin drywall hanging.
 - Place stockpiled excavated soil as backfill beneath designated Parcel 2 parking areas.
 - Begin Garage 2 grade preparation for foundations. Vapor barrier installation anticipated to begin September 9. Aspect will keep DEQ apprised of schedule.

UPCOMING DELIVERABLES to DEQ and ACTION ITEM REQUESTS

- Aspect's semiannual groundwater monitoring report was submitted to DEQ on August 18.

PHOTOS

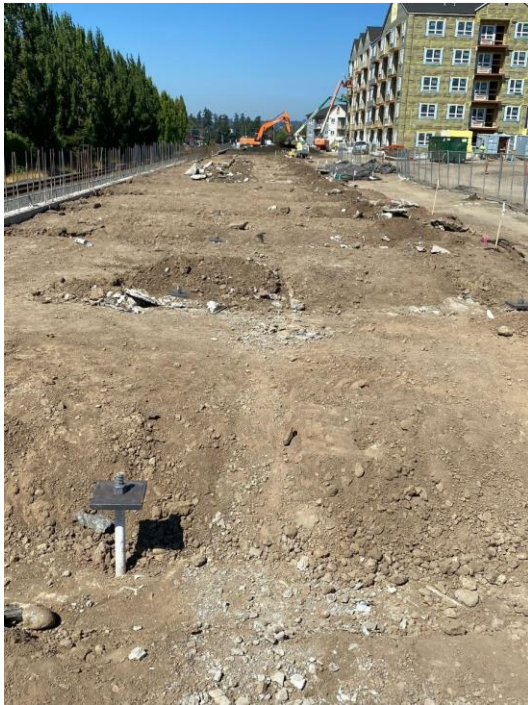

9/1/22 Garage 2 micropiles on Parcel 2, looking west.



9/1/22 Excavated stockpiled utility trench soil, prior to covering with visqueen, looking south on Parcel 2 towards exclusion zone.
