



Aspect Weekly Update

Seven Acres Development (Former LDM Site - ECSI #887)

WEEK 48: SEPTEMBER 12 - SEPTEMBER 16, 2022


ON-SITE ACTIVITIES

- Continue ROW electrical work.
- Parcel 1:
 - Continued backfilling Garage 1 and NE Retaining Wall. Began Garage 1 building pad preparation.
 - Continued constructing Buildings 1, 2, 3, and 4.
 - Continued preparing Building 5 for concrete pour. Began Building 5 slab-on-grade pour.
- Parcel 2:
 - Continued Clubhouse MEP rough-ins. Completed fireplace insert.
 - Continued preparing Garage 2 grade for vapor barrier installation. Continued Garage 2 vapor barrier installation.
 - Continued utility trenching.
 - Began burying utility trenched soil in front of Garage 2.
 - Holt Services adjusted (lowered) monitoring wells DMW-10, IMW-10, VDMW-14, and DMW-14 on 9/12.
 - No waste was transported off site this week.
- Aspect was on site on September 12, 15, and 16 to observe well adjustments, Garage 2 vapor barrier installation, and utility trenching.

- Point Environmental was on site on September 14 to inspect erosion control measures.
- DEQ was on site on September 16 to observe site progress and Garage 2 vapor barrier installation.

PLAN VIEW PROGRESS

Parcel 2 construction work focused on monitoring well adjustments, Garage 2 grade preparation, Garage 2 vapor barrier installation, utility trenching, and utility trench stockpile soil burial.

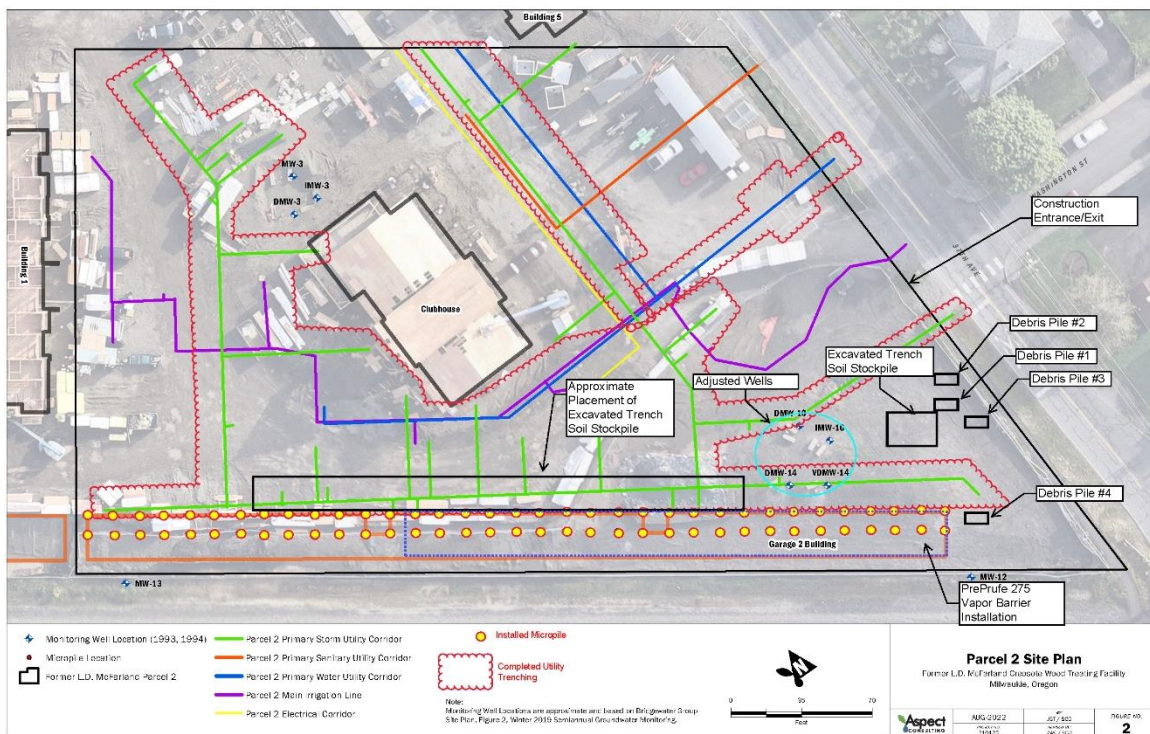

KEY ONSITE ACTIVITIES PLANNED FOR NEXT TWO WEEKS

- Begin ROW signage, striping, electrical conduits, and asphalt multi-use pavement.
- Parcel 1:
 - Continue Garage 1 backfill and building pad preparation. Begin concrete foundations.
 - Continue constructing Building 1, 2, 3, and 4.
 - Continue Building 5 slab-on-grade pour. Begin wall framing and floor joists for Building 5.
- Parcel 2:
 - Continue Clubhouse MEP rough-ins. Begin siding and insulation.
 - Continue Parcel 2 utility trenching.

- Continue placing stockpiled excavated soil as backfill beneath area in front of Garage 2 and designated Parcel 2 parking areas.
- Continue Garage 2 vapor barrier installation. Begin Garage 2 concrete foundations installation. Aspect will keep DEQ apprised of schedule.

UPCOMING DELIVERABLES to DEQ and ACTION ITEM REQUESTS

- None.

PHOTOS



9/15/22 Adjusted Parcel 2 wells DMW-10, IMW-10, VDMW-14, and DMW-14 protected by ecology blocks and barricades.



9/15/22 Parcel 2 Garage 2 PrePrufe vapor barrier membrane installation progress.
