



Aspect Weekly Update

Seven Acres Development (Former LDM Site - ECSI #887)


WEEK 49: SEPTEMBER 19 - SEPTEMBER 23, 2022

ON-SITE ACTIVITIES

- Continue ROW electrical work.
- Began Phase 1 paving. Prepared and poured curbs.
- Parcel 1:
 - Continued Garage 1 building pad preparation.
 - Continued constructing Buildings 1, 2, 3, and 4.
 - Completed Building 5 slab-on-grade final pour.
- Parcel 2:
 - Continued Clubhouse MEP rough-ins.
 - Continued Garage 2 vapor barrier installation.
 - Continued utility trenching. Continued burying utility trenched soil between Garage 2 and Clubhouse.
 - No waste was transported off site this week.
- Aspect was onsite on September 20.

PLAN VIEW PROGRESS

Parcel 2 construction work focused on Garage 2 vapor barrier installation, utility trenching, and utility trench stockpile soil burial and temporary pavement capping between Garage 2 and the Clubhouse.

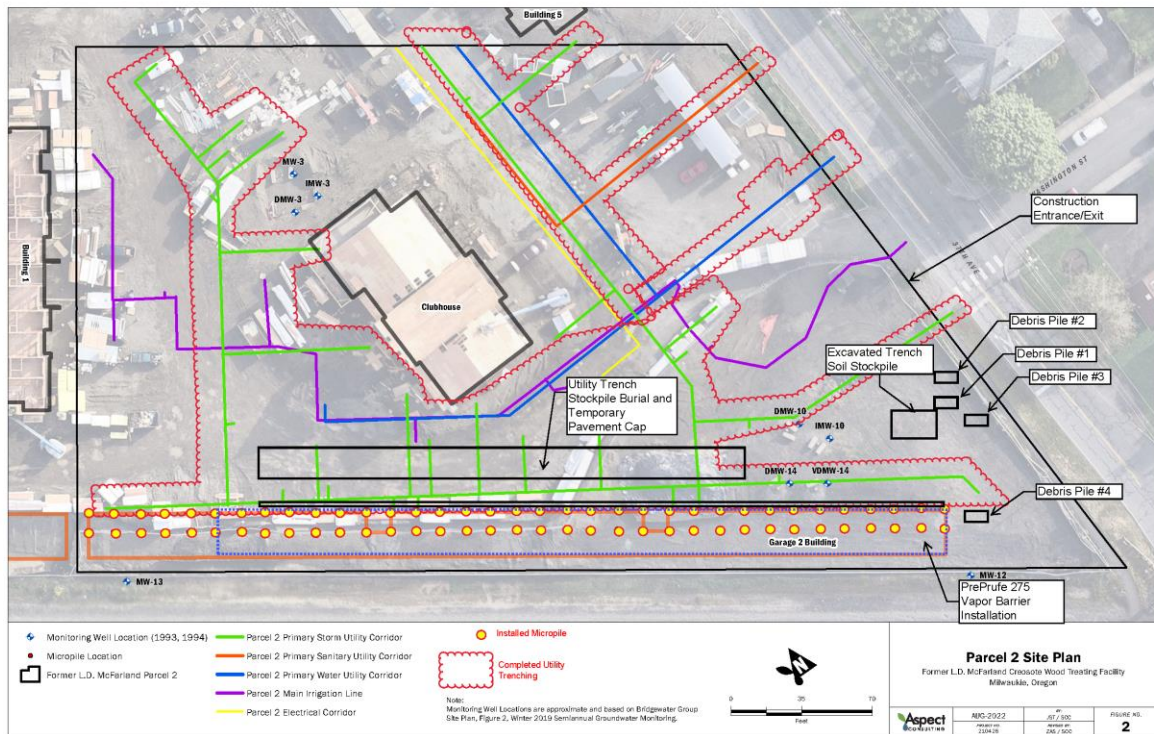

KEY ONSITE ACTIVITIES PLANNED FOR NEXT TWO WEEKS

- Continue ROW electrical work. Begin ROW PGE light poles and street asphalt.
- Parcel 1:
 - Begin Garage 1 concrete foundations.
 - Continue Buildings 1, 2, 3, and 4 construction.
 - Begin Building 5 wall framing and floor joists.
- Parcel 2:
 - Continue Clubhouse MEP rough-ins. Continue fireplace insert. Begin siding, insulation, and drywall hanging.
 - Continue utility trenching.

- Continue burying utility trench stockpiled soil on Parcel 2 between Garage 2 and Clubhouse and in SE parking area E of Garage 2.
- Continue Garage 2 vapor barrier installation. Begin Garage 2 concrete foundations installation. Aspect will keep DEQ apprised of schedule.

UPCOMING DELIVERABLES to DEQ and ACTION ITEM REQUESTS

- None.

PHOTOS



9/22/22 Parcel 2 Garage 2 PrePrufe vapor barrier membrane rebar penetration tie-in.



9/21/22 Parcel 2 4-inch temporary, clean backfill pavement cap over utility trench stockpile soil buried between Garage 2 footprint (left) and Clubhouse (right), viewing west.
