



## Aspect Weekly Update

Seven Acres Development (Former LDM Site - ECSI #887)


WEEK 50: SEPTEMBER 26 - SEPTEMBER 30, 2022

### ON-SITE ACTIVITIES

- Continue ROW electrical work. Began Phase 1 paving. Prepared and poured curbs.
- Parcel 1:
  - Continued Garage 1 building pad preparation.
  - Continued constructing Buildings 1, 2, 3, and 4.
  - Began Building 5 wall framing.
- Parcel 2:
  - Continued Clubhouse MEP rough-ins.
  - Began Garage 2 building pad preparation for slab-on-grade pour.
  - No waste was transported off site this week.
- Aspect was not onsite this week.
- Point Environmental was on site on 9/28 to inspect erosion control measures.

# PLAN VIEW PROGRESS

Parcel 2 construction work focused on Garage 2 building pad preparation and utility trenching.

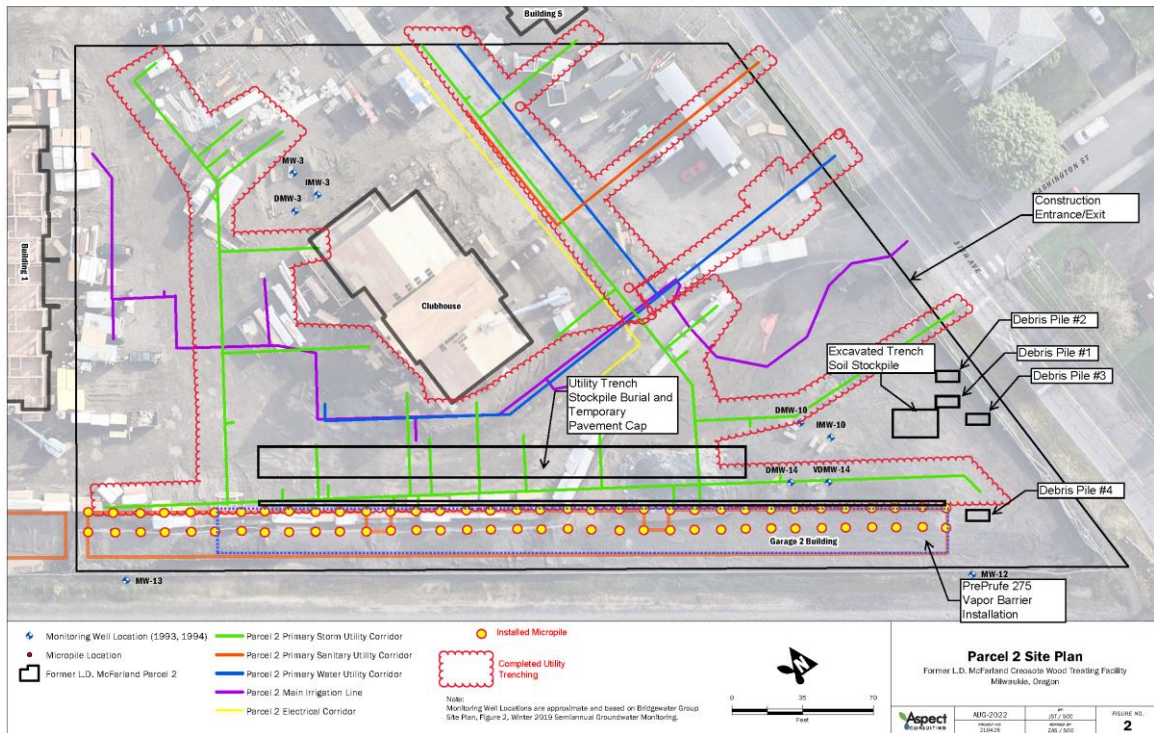

## KEY ONSITE ACTIVITIES PLANNED FOR NEXT TWO WEEKS

- Continue ROW electrical work and street asphalt.
- Begin electrical conduit installation.
- Parcel 1:
  - Continue Garage 1 concrete foundations.
  - Continue Buildings 1, 2, 3, 4 and 5 construction.
- Parcel 2:
  - Continue Clubhouse MEP rough-ins. Continue fireplace insert. Begin siding, insulation, and drywall hanging.
  - Continue Parcel 2 utility trenching and stockpiling trench soil until additional soil burial location is identified.
  - Begin pavement subgrade prep of utility trench soil buried between Garage 2 and Clubhouse.

- Continue Garage 2 vapor barrier installation. Begin Garage 2 concrete pour and grade prep for slab-on-grade. Aspect will keep DEQ apprised of schedule.

## UPCOMING DELIVERABLES to DEQ and ACTION ITEM REQUESTS

- None.

## PHOTOS



9/30/22 Parcel 2 Garage 2 build pad preparation, viewing northwest.



9/30/22 Parcel 2 Garage 2 build pad preparation. Rebar installed over PrePrufe vapor barrier, viewing south.
