



## Aspect Weekly Update

Seven Acres Development (Former LDM Site - ECSI #887)


WEEK 51: OCTOBER 3 - OCTOBER 7, 2022

### ON-SITE ACTIVITIES

- Continue ROW electrical, curbs, sidewalks and approaches.  
Began ROW street asphalt.
- Continued Phase 1 paving.
- Parcel 1:
  - Continued Garage 1 building pad preparation.
  - Continued constructing Buildings 1, 2, 3, 4 and 5.
- Parcel 2:
  - Continued Clubhouse MEP rough-ins, insulation, and fireplace insert.
  - Poured Garage 2 slab-on-grade.
  - No waste was transported off site this week.
- Aspect was onsite on 10/3 and 10/6.
- DEQ was onsite on 10/3.

# PLAN VIEW PROGRESS

Parcel 2 construction work focused on Garage 2 slab pour.

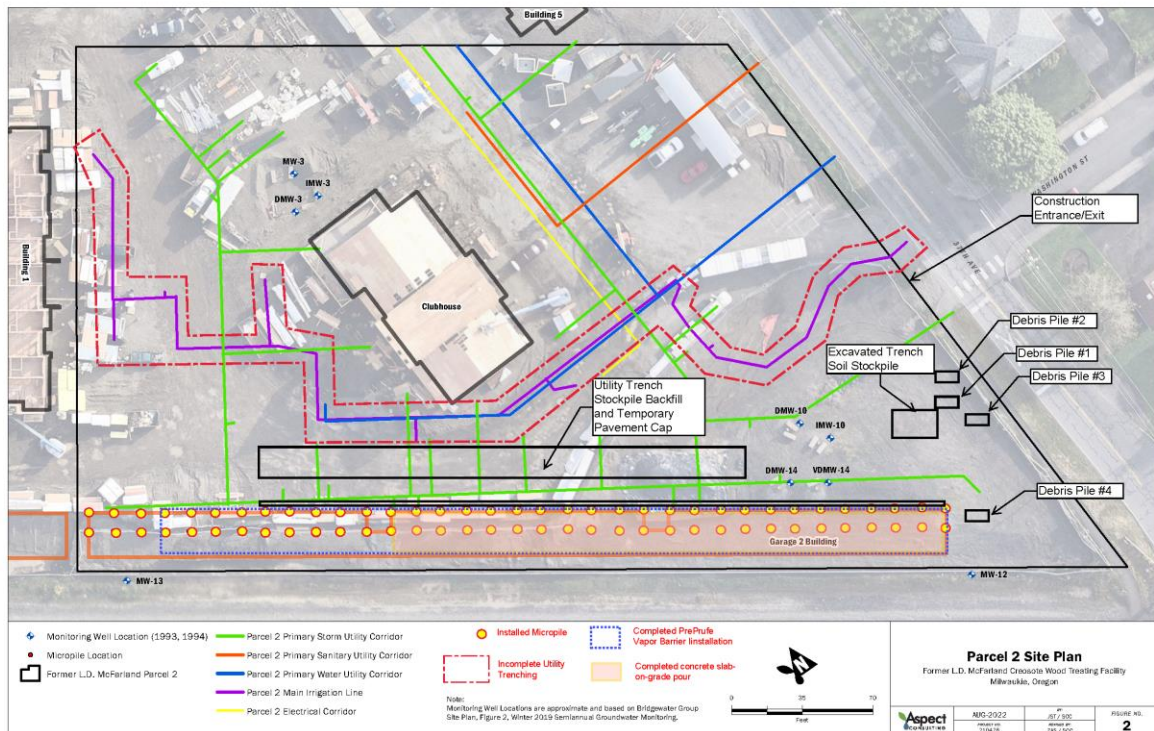

## KEY ONSITE ACTIVITIES PLANNED FOR NEXT TWO WEEKS

- Continue ROW electrical work, street asphalt pavement, signage and striping.
- Continue Phase I paving. Begin electrical conduit installation.
- Parcel 1:
  - Continue Garage 1 slab-on-grade pour preparation.
  - Continue Buildings 1, 2, 3, 4 and 5 construction.
- Parcel 2:
  - Continue Clubhouse insulation and fireplace insert. Begin siding and drywall work.
  - Begin site electrical conduit utility trenching. Stockpile trench soil prior to onsite burial.
  - Continue subgrade pavement prep in trench soil backfill, between Garage 2 and Clubhouse.

- Continue Garage 2 vapor barrier installation. Continue grade prep for second slab-on-grade pour. Aspect will keep DEQ apprised of schedule.

## UPCOMING DELIVERABLES to DEQ and ACTION ITEM REQUESTS

- None.

## PHOTOS



10/3/22 Parcel 2 Garage 2 rebar over vapor barrier prior to slab-on-grade pour, viewing northwest.



10/6/22 Parcel 2 Garage 2 slab-on-grade pour, viewing west.
