



## Aspect Weekly Update

Seven Acres Development (Former LDM Site - ECSI #887)

WEEK 52: OCTOBER 10 - OCTOBER 14, 2022


### ON-SITE ACTIVITIES

- Continue ROW electrical.
- Continue Phase 1 paving.
- Parcel 1:
  - Continue Garage 1 building pad preparation.
  - Continue constructing Buildings 1, 2, 3, 4 and 5.
- Parcel 2:
  - Continue Clubhouse MEP rough-ins and fireplace insert. Begin siding.
  - Prepare Garage 2 slab-on-grade for second pour. Complete vapor barrier installation.
  - Bury trench soil stockpile in parking south of Clubhouse.
  - No waste was transported off site this week.
- Aspect was not onsite this week.

- Point Environmental was on site on 10/10 to inspect erosion control measures.

## PLAN VIEW PROGRESS

Parcel 2 construction work focused on trench stockpile soil burial and Garage 2 vapor barrier installation and slab pour preparation.

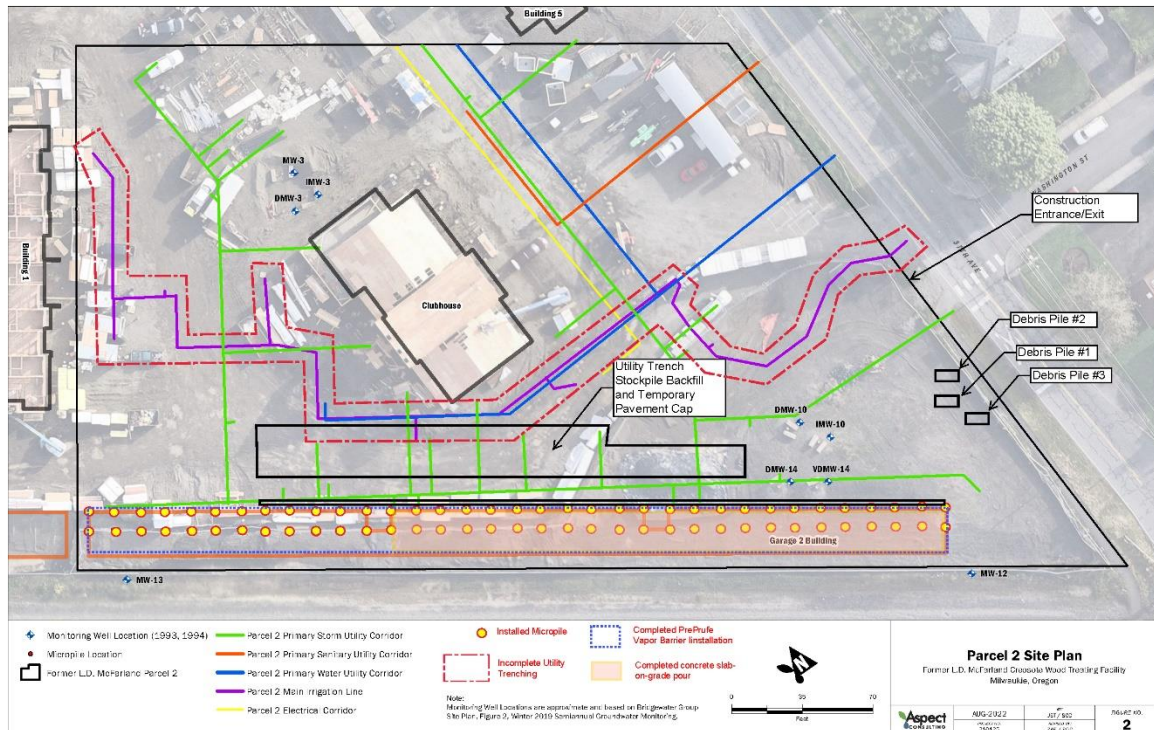

## KEY ONSITE ACTIVITIES PLANNED FOR NEXT TWO WEEKS

- Continue ROW electrical work. Being irrigation mains.
- Continue Phase I paving.
- Parcel 1:
  - Garage 1 slab-on-grade pour. Begin wood framing.
  - Continue Buildings 1, 2, 3, 4 and 5 construction.
- Parcel 2:
  - Continue Clubhouse MEP rough-ins, insulation and siding. Begin drywall hanging.
  - Begin site electrical conduit utility trenching.
  - Begin tree well excavation.

- Continue burying trench and tree well soil between Garage 2 and Clubhouse. Prepare pavement subgrade over backfill.
- Continue Garage 2 grade prep and rebar installation for second slab-on-grade pour. Pour is anticipated Tuesday, 10/18. Notification of pour schedule provided to DEQ.

## UPCOMING DELIVERABLES to DEQ and ACTION ITEM REQUESTS

- None.

## PHOTOS



10/14/22 Parcel 2 Garage 2 set slab-on-grade concrete (poured last week), viewing northwest.



10/14/22 Parcel 2 Garage 2 vapor barrier installation, viewing south.
